


- Seminar in Vienna, 05.06.2018
- Group work with Swimlane Process Chart
- SMART COMMUTING | Vienna University of Technology



Time



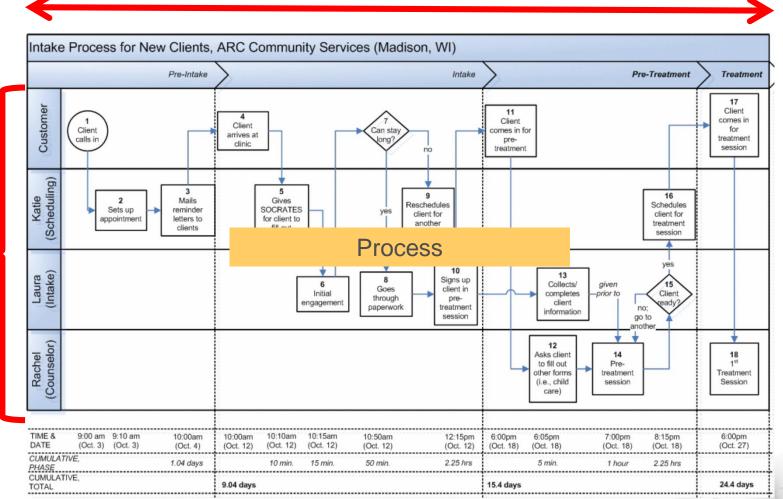

Organization or

Personnel

Quelle: CHESS/NIATx, University of Wisconsin-Madison

TAKING COOPERATION FORWARD















Timeline





Timeline

Tasks of Stakeholder 1
Tasks of Stakeholder 2
•••



TRANSIT-ORIENTED DEVELOPMENT + IMPROVEMENT RAILWAY STATION (1)



Ministry A		Subsidy approva		Technica Approval
Railway IM			Participation Technical Design	Renovation Railway Station
Mun. Council			Budget Approval	
Municipality	Initial idea	Idea competition	Contract Land + Dvlpmt	Renovation Station Square
PT Operator			Participation Technical Design	
Land owners	Selling land			
Real Estate Developers				Real estate development
General Public			Participation process	
-			TAKING COOPERATION	FORWARD 7

TRANSIT-ORIENTED DEVELOPMENT


+ IMPROVEMENT RAILWAY STATION (2)



٨	Month (0	Month X		Month Y
Ministry A		Subsidy approval			Technica Approval
Railway IM			Participation Technical Design		Renovation Railway Station
Mun. Council			Budget Approval		
Municipality	Initial idea	ldea competition	Contrac Land +	t Ivlpmt.	Renovation Station Square
PT Operator			Participation Technical Design		
Land owners				Selling la	and
Real Estate Developers					Real estate development
General Public			Participat process	on	
			— TAKING COOPER	R <mark>ATION</mark> FO	RWARD 8

A COMPLICATED EXAMPLE



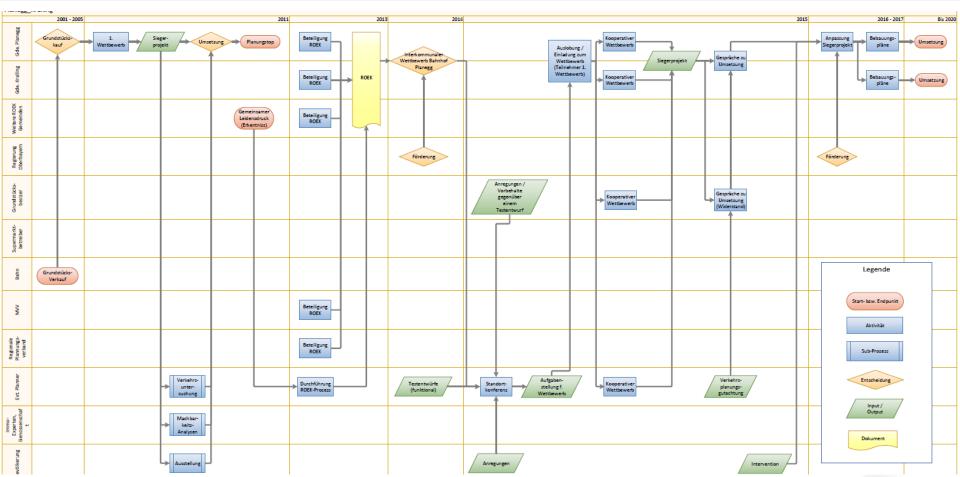





Flipchart & Post-it Method









Tasks

- Select 1 measure that you want to focus on in order to make commuting more sustainable (Remember: Transnational Strategy);
- 2. Think about who will be stakeholders in the process, and write down with post it.
- 3. Then, let us get started:
 - What is the starting point?
 - □ What process is needed?
 - □ Which stakeholder is responsible for it?
 - □ What is the time needed for each process?
- 4. At the end: present it to the others

